

Software Engineering Lab-2

PES1UG24CS401 - Saiesh Shankar

This is the creation of the Main board - beginning of first sprint.

Sprint - 1

Start Sprint

×

2 work items will be included in this sprint.

Required fields are marked with an asterisk *

Sprint name *

Duration *

1 week

Start date *

8/26/2026 9:05 PM

Date format: MM/DD/YYYY. Time format: e.g. 1:00 PM.

End date *

9/2/2026 9:05 PM

Sprint goal



Let's have fun and build this thing!

CancelStart

Sprint 2 :

MRA Sprint 2 2 Sep – 9 Sep (2 work items)				13	0	0	Start sprint	...
☒ MRA-6	Story 2.1: Submit Loan Request	MRA Sprint - 2	To Do	5				
☒ MRA-7	Story 2.2: View & Fund Loan	MRA Sprint - 2	To Do	8				
+ Create								

Burn Down Chart :

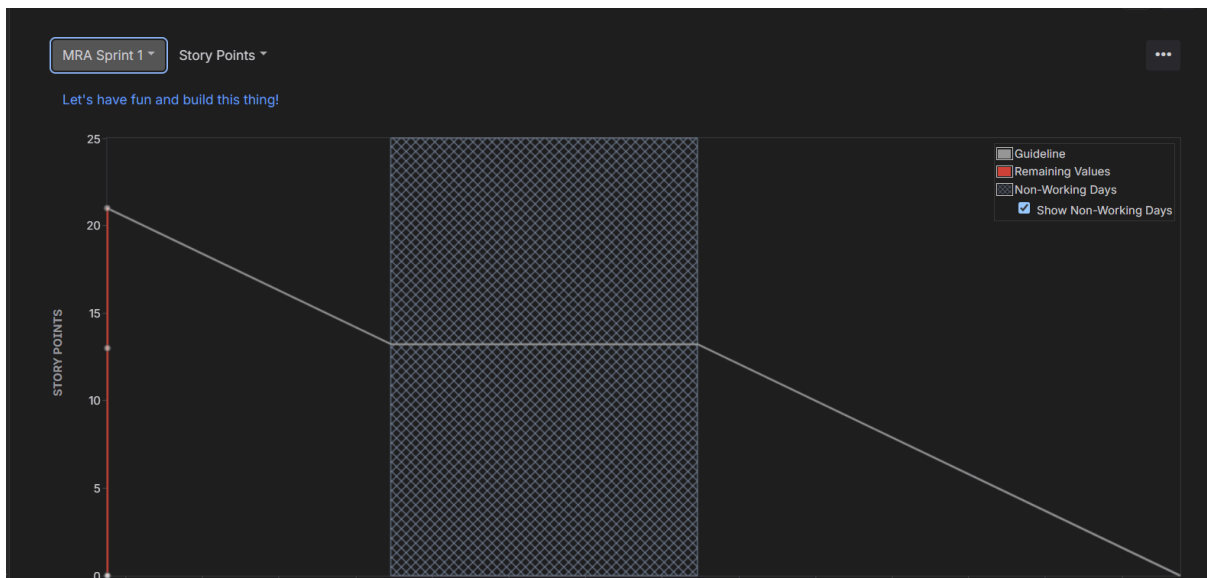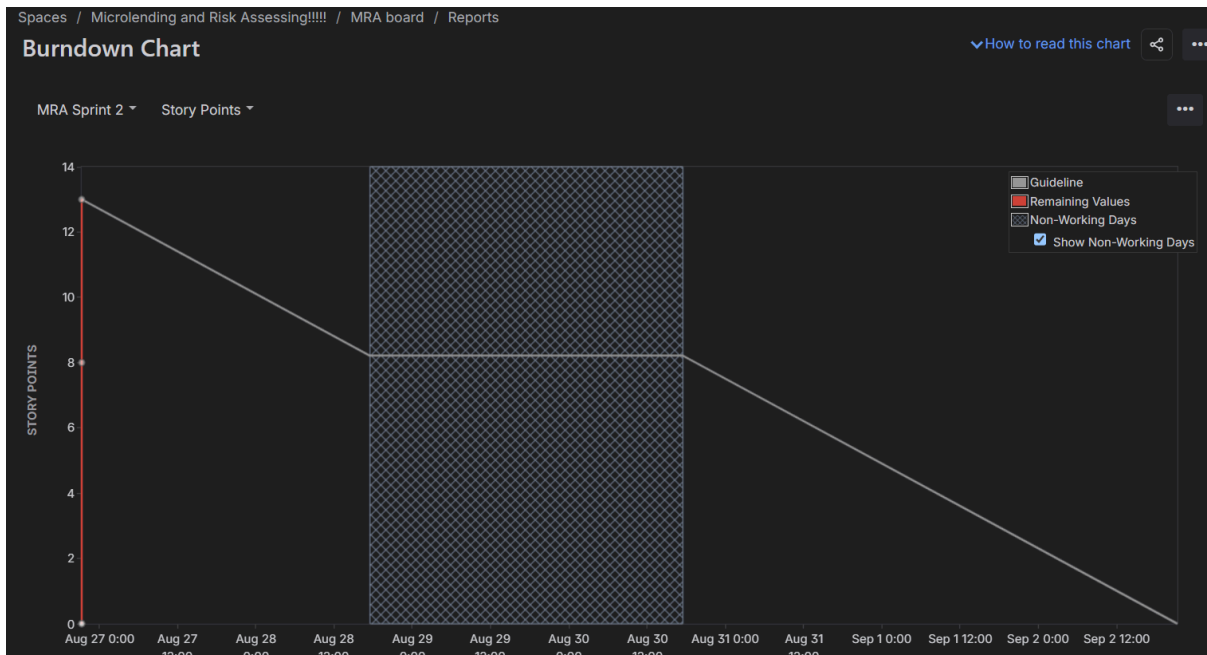

1. Did your estimations reflect the actual effort?

Ans : Since this was a simulated sprint executed during a short lab session, the physical time spent did not match real-world hours. However, the use of the Fibonacci sequence accurately reflected the *relative* complexity of the tasks. For example, assigning a higher point value to the "Risk Rating Computation" accurately represented the heavier logic required compared to the lower-effort "Submit Loan Request" form.

2. Was your backlog well-prioritized?

Ans :

Yes, the backlog was logically prioritized based on functional dependencies. Foundational tasks, such as creating the Borrower's financial profile and computing their risk rating, were placed at the top of the backlog with the highest priority. This ensured that downstream user stories, which strictly require a valid risk rating before a loan can be submitted or funded, were not blocked.

3. How did your simulated sprint align with your plan?

Ans : The simulated sprint aligned perfectly with the initial plan. All the user stories committed to Sprint 1 (focusing on Borrower Onboarding and Assessment) were successfully transitioned from "To Do," to "In Progress," and finally to "Done". This allowed the sprint goal to be met within the simulated timeframe without any scope creep.

4. What insights did the burndown chart give about your team's capacity?

Ans : Because the tasks were completed rapidly during the lab simulation, the actual remaining values (the red line) on the burndown chart showed a very sharp drop compared to the linear, gradual decline of the guideline (the grey line). In a real-world scenario, finishing work this early below the guideline would indicate that the team either overestimated the complexity of the tasks or did not commit to enough work during sprint planning, suggesting that the team has the capacity to take on more story points in Sprint 2.
